
Northstar · actual portfolio and proposed next week

13 project containers · 186 actual work packages · 83 observed relations. Source 2026-11-07T09:14:26.576Z.

All date positions are illustrative review / decision windows, not native dates, forecasts, effort estimates or commitments.

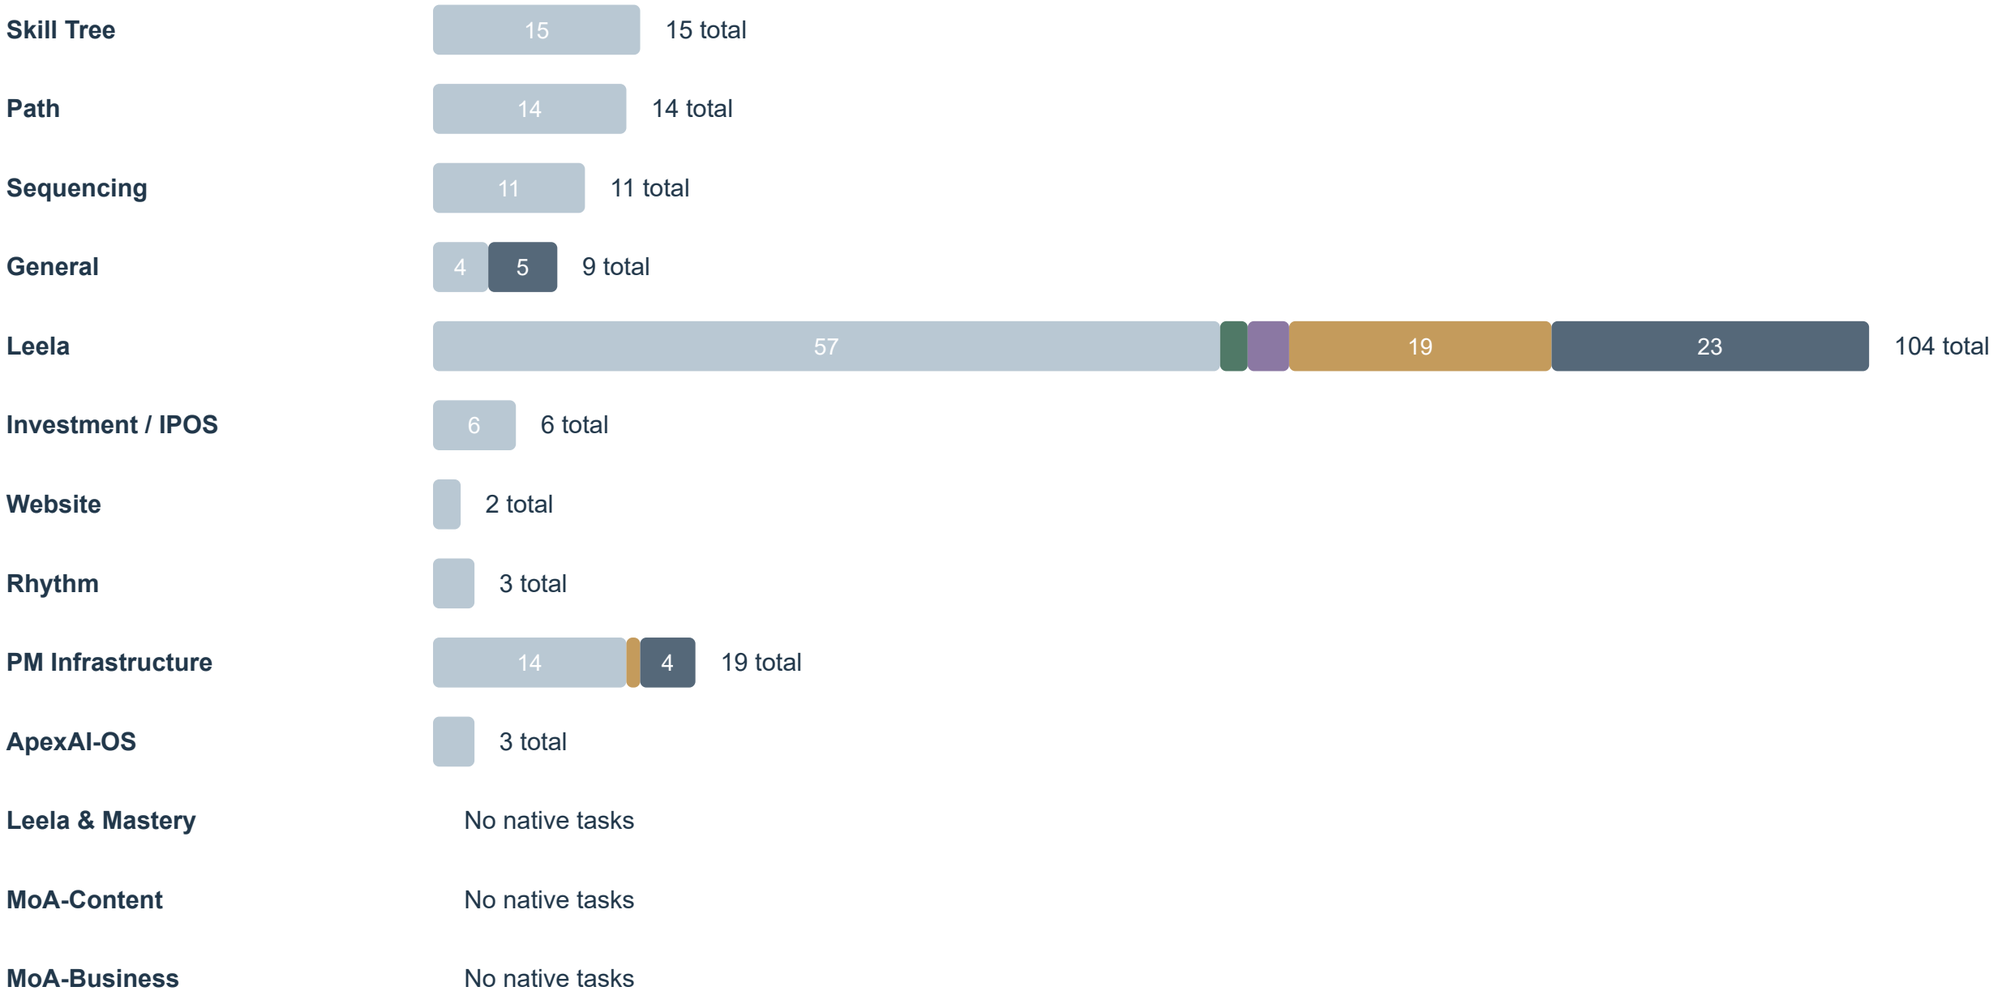

Next week · 9–15 November 2026

An alternative focus scenario. Operator capacity has not been checked. Sunday is off.

Monday · 09 Nov	Tuesday · 10 Nov	Wednesday · 11 Nov	Thursday · 12 Nov	Friday · 13 Nov	Saturday · 14 Nov	Sunday · 15 Nov
Runtime reliability	**Identity & placement**	**Website content**	**IPOS operations**	**Sequencing readiness**	**Rhythm evidence / review**	**Off**
Proposed focus	Proposed focus	Alternative focus	Alternative focus	Proposed focus	Alternative focus	No work planned
Review current completion / timer failures; select a bounded gap.	Inspect canonical identity and the placement decision.	Review one authentic source-to-public-content slice.	Inventory working assets before choosing a bounded benchmark.	Reconcile landed claims; bound the remaining C3 objective.	Re-attest one boundary, then review what to carry forward.	Off by default.
#211 #212	#159 #187 #188	#163	#228 #225	#216 #217 #218	#174	

What the Gantt means

- Dates are illustrative review/decision windows, not native dates, effort estimates or commitments.
- Parallel windows do not imply the operator can execute every lane concurrently.
- Downstream windows are conditional on accepted prerequisite evidence.
- The seven-day board is an alternative focus scenario; choose/reduce it against actual capacity.
- No source task status, priority or dependency has been changed.


Hatched bars are proposed windows; native states remain unchanged.

Dependency atlas

Solid: observed requires / follows. Grey dotted: ownership. Purple dashed: proposed interpretation. Blue dashed: association.


Identity unlocks two project areas

Skill Tree → Path. Solid requires edges are native prerequisites; grey ownership edges are not blockers.

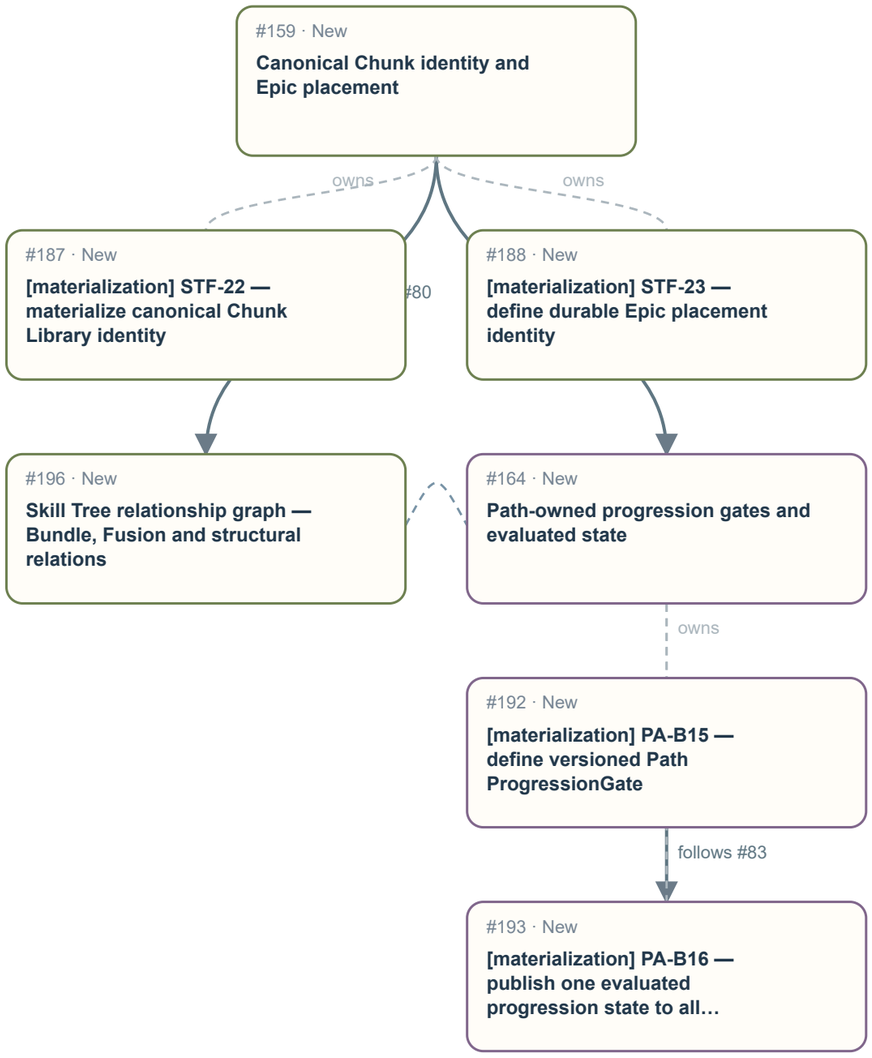

Runtime reliability and release acceptance

#207 is PM-closed; current acceptance evidence still needs review. Blue relates edges do not imply blockers.

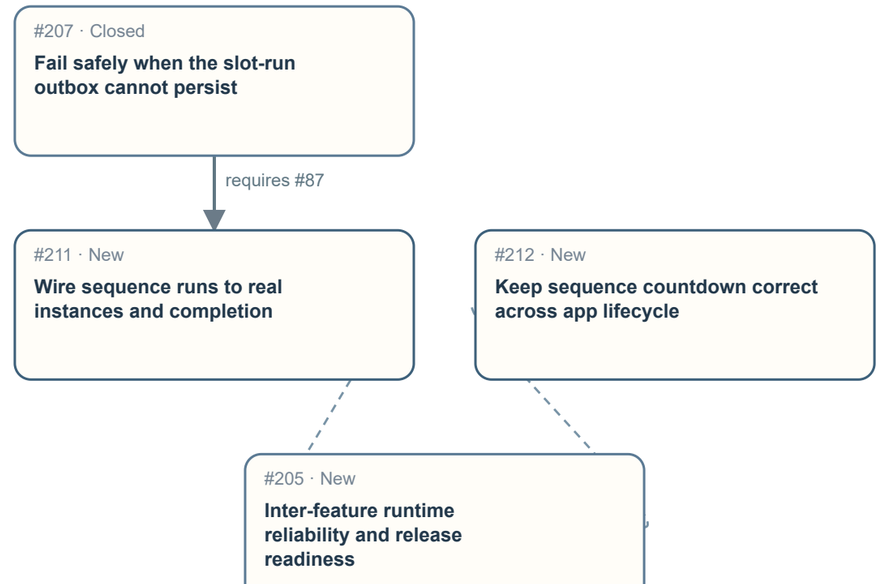


Dependency atlas

Solid: observed requires / follows. Grey dotted: ownership. Purple dashed: proposed interpretation. Blue dashed: association.

Home / Skill Tree: branches and a join

Leela. Observed follows edges preserve the actual parallel branches and integration order.

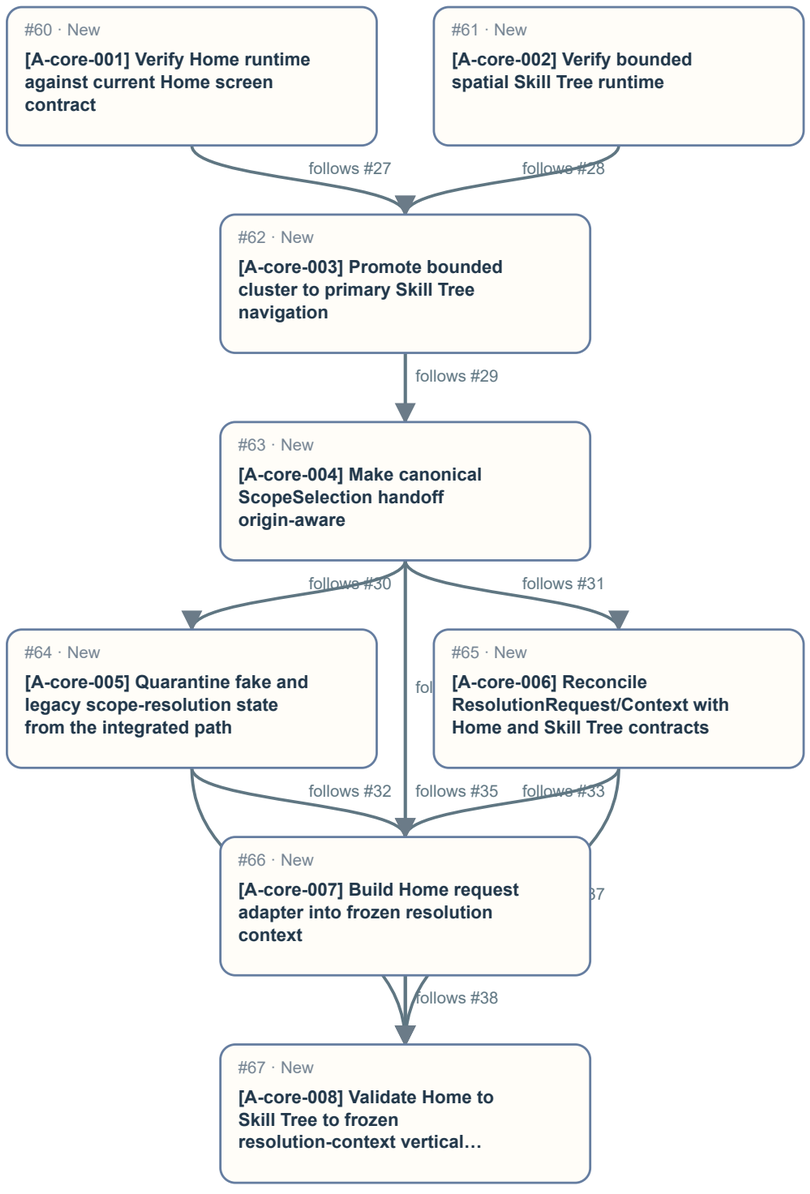

Sequencing: ordering and status conflict

All five native states are New. Descriptions say landed or BLOCKED; reconcile them before execution.



Dependency atlas

Solid: observed requires / follows. Grey dotted: ownership. Purple dashed: proposed interpretation. Blue dashed: association.


IPOS: inventory and parallel intake goals

Purple dashed ordering is a proposal. No native dependency is invented between the other goals.



PM Infrastructure: human approval gate

All arrows are proposed workflow interpretation. #128 is actually On hold; approval is not assumed.

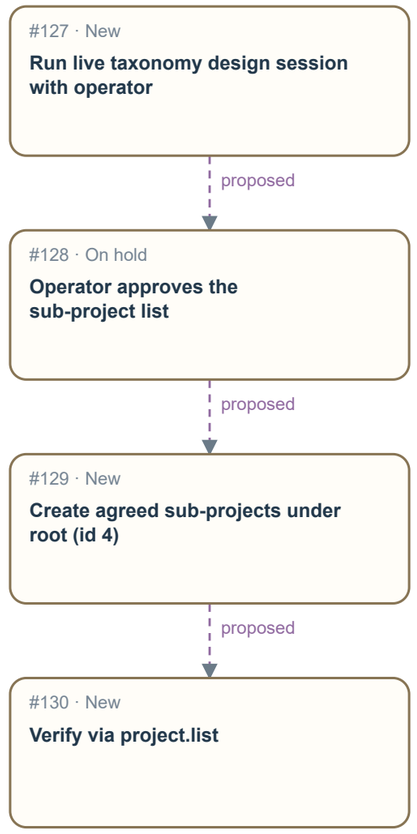

Dependency atlas

Solid: observed requires / follows. Grey dotted: ownership. Purple dashed: proposed interpretation. Blue dashed: association.

Website: two actual goals

No native dependency is recorded between Content Transformation and the separate credits page.

#163 · New

Content Transformation

#204 · New

ACIM Secular: Dedicated Sources & Commentary Credits Page (Sean Reagan, Dr. Kenneth Wapnick /…

Rhythm: independent review candidates

No native serial edges between these three tasks. Gantt dates are illustrative review windows only.

#174 · New

[materialization] RH-B02 — re-attest BP evidence boundary

#175 · New


[materialization] RH-B10 — re-attest visible planning metrics

#176 · New

[materialization] RH-B21 — re-attest weekly fit feedback

Four-week Gantt · Leela product lanes


Illustrative windows; all dependent work is conditional on prerequisite acceptance. 9 November – 6 December.

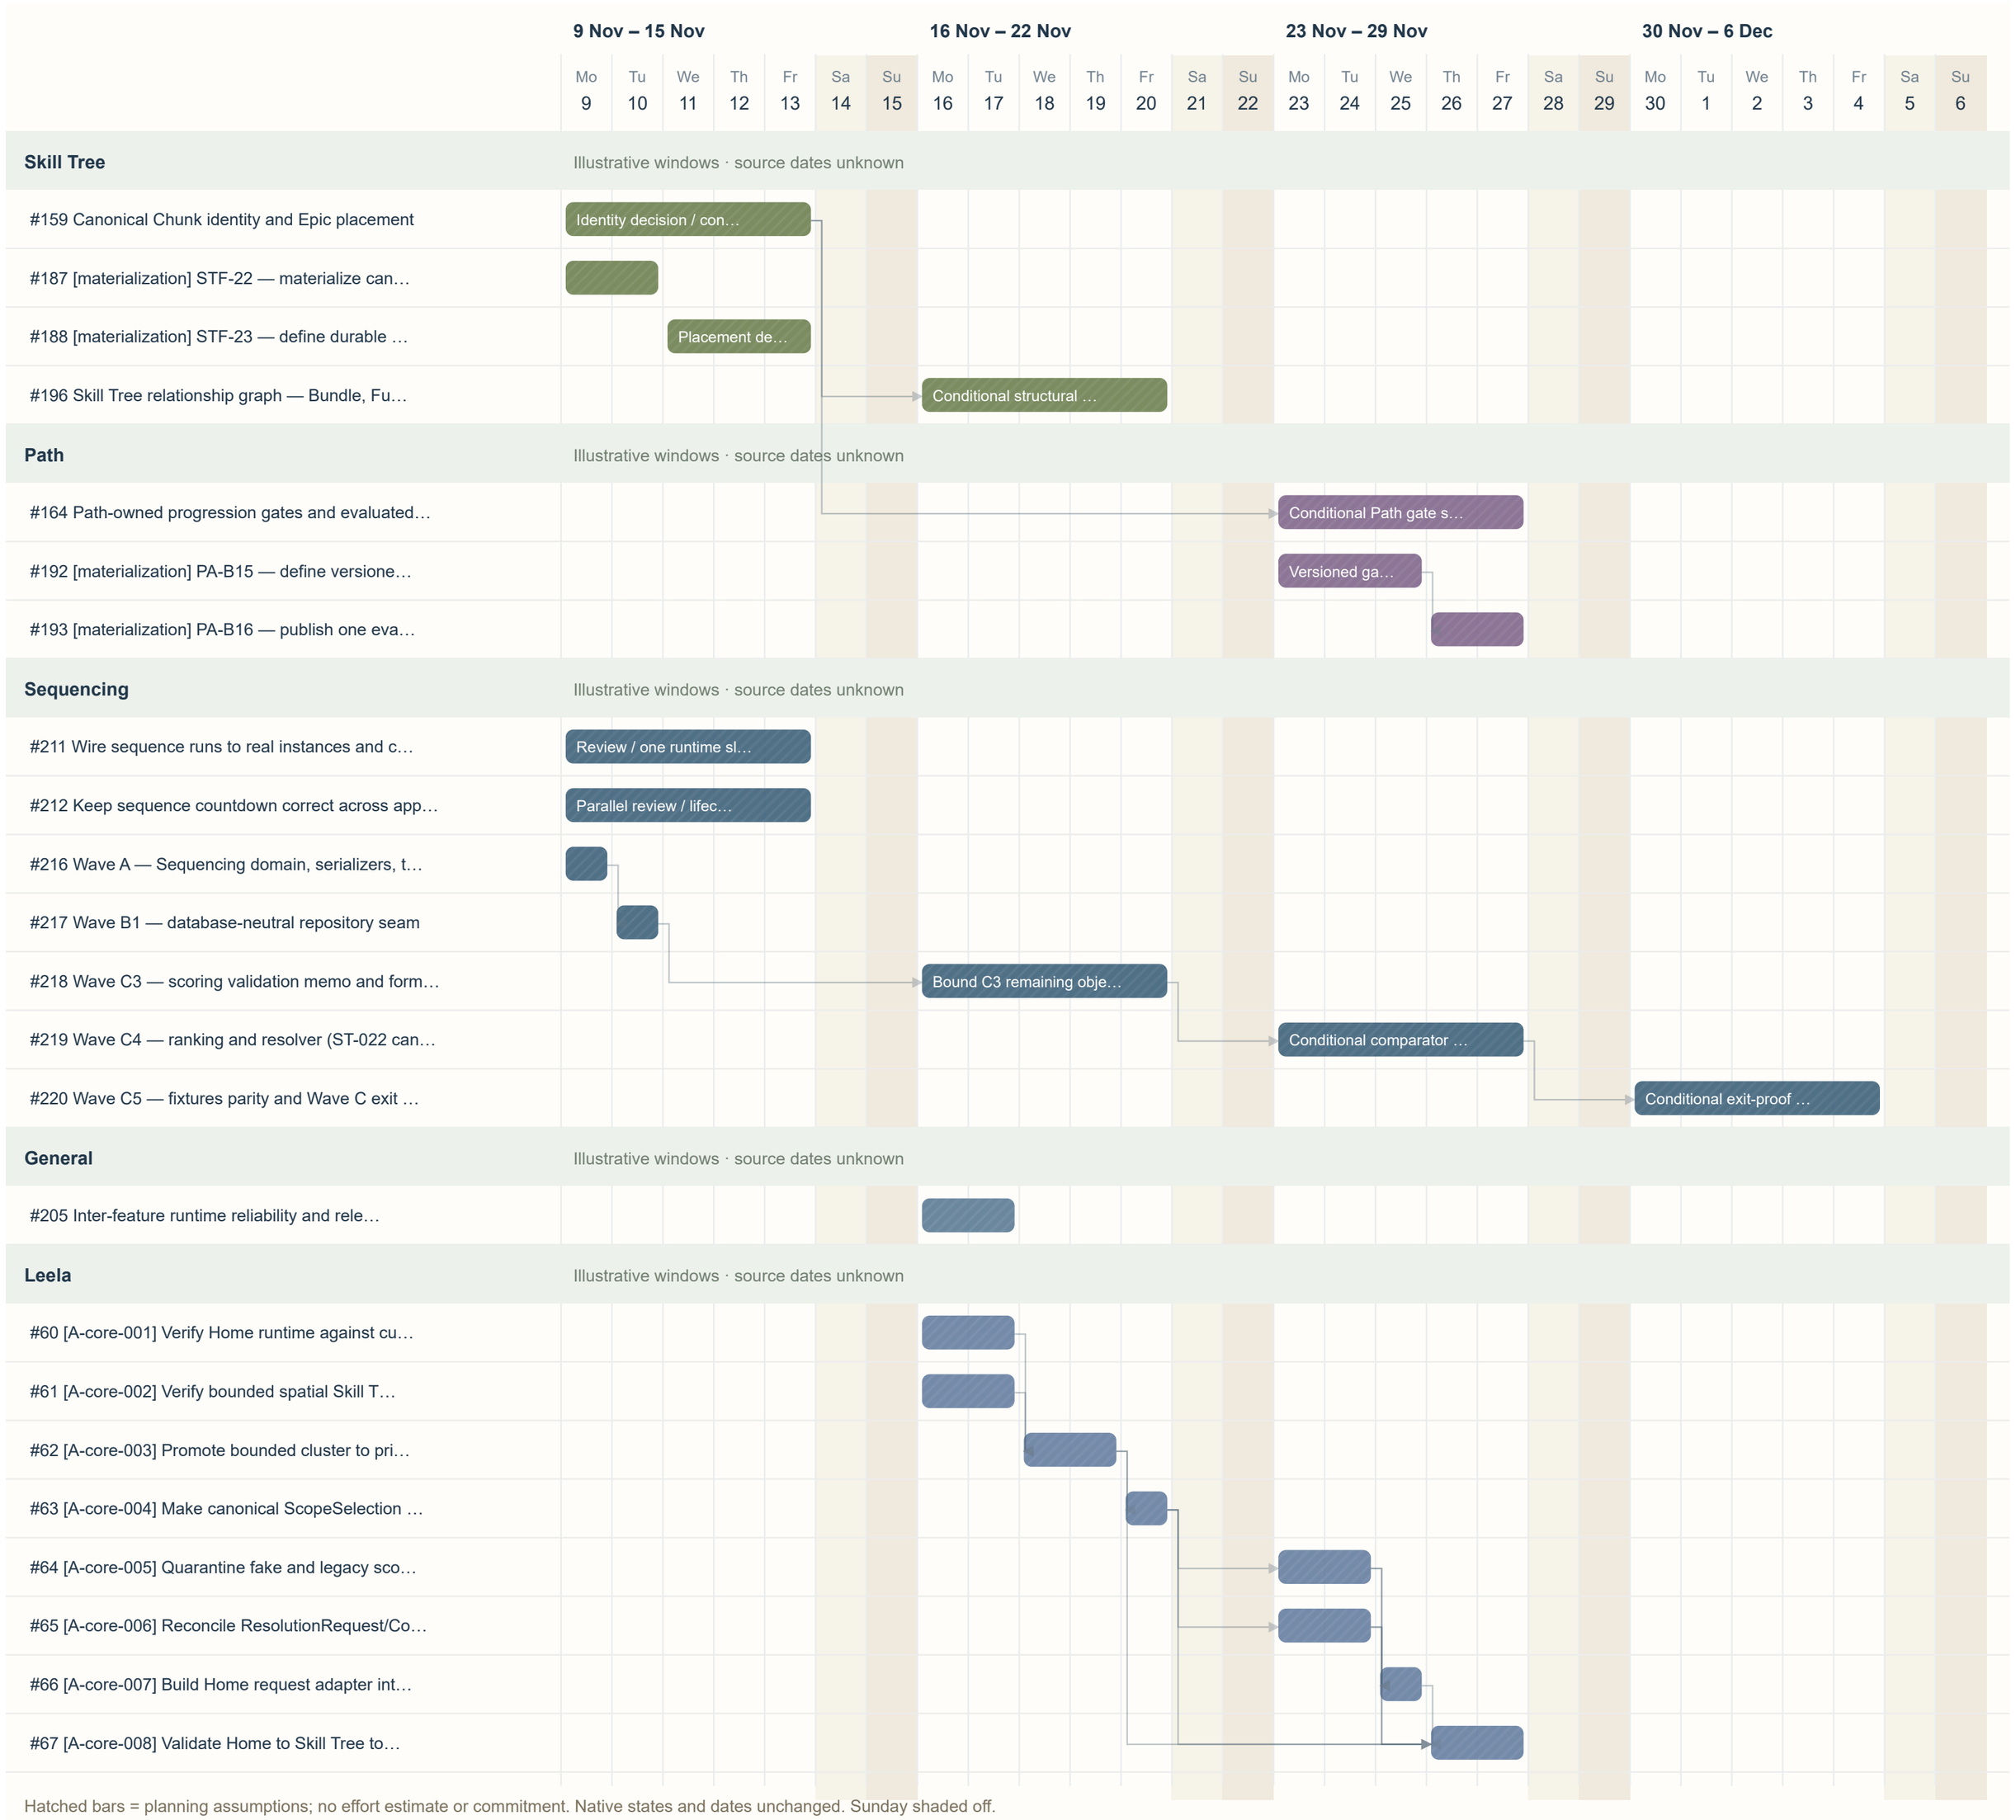

Hatched bars = planning assumptions; no effort estimate or commitment. Native states and dates unchanged. Sunday shaded off.

Four-week Gantt · operations, content and portfolio lanes

Illustrative windows; empty native containers stay empty. Native dates and commitments are unchanged.

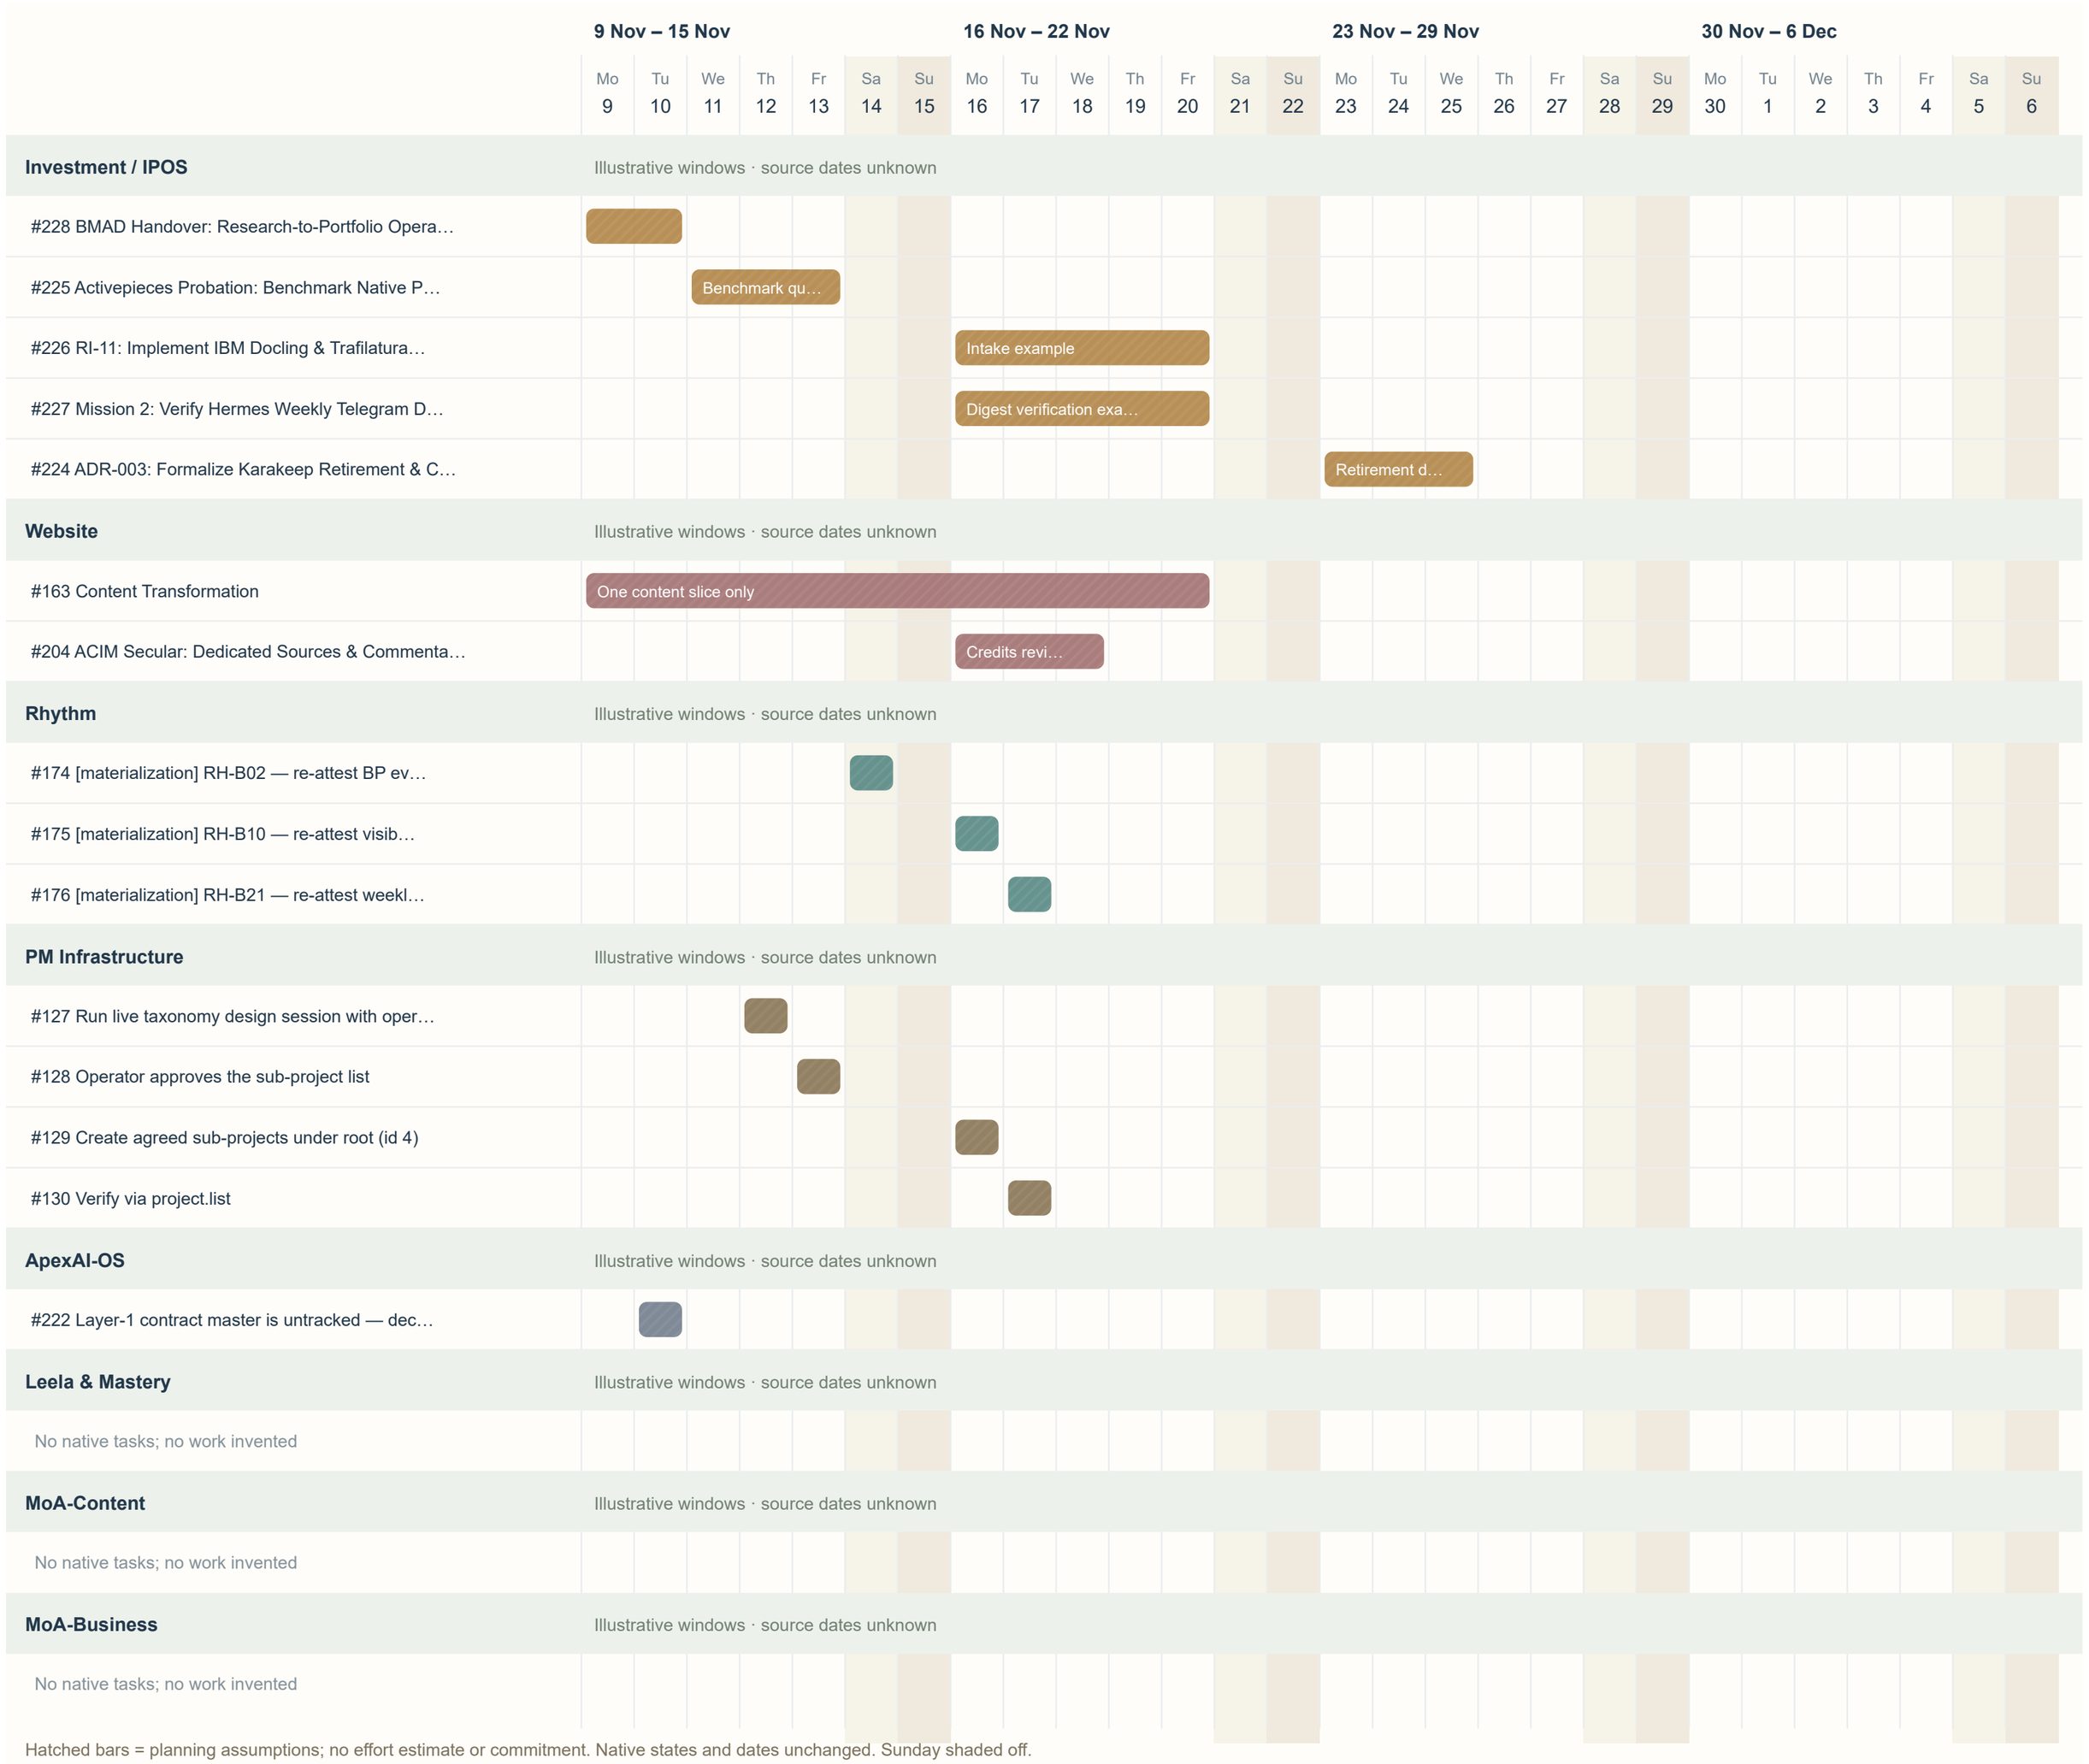

Hatched bars = planning assumptions; no effort estimate or commitment. Native states and dates unchanged. Sunday shaded off.
